2018-19

THIRD PARTY INSPECTION REPORT

Name of the Client : **Executive Engineer,**
Electrical- Yelahanka Zone,
BBMP, Bangalore.

Name of Agency : **Executive Engineer-3,**
KRIDL, Bangalore.

Name of the Work : Providing Path Way Lighting to Bhuvaneshwarinagar Park in Ward No.06, BBMP, Bangalore.

Estimated Cost - Rs. 10.00 Lakhs

THIRD PARTY INSPECTION CONSULTANTS

CIVIL QUALITY CONSULTANTS AND ENGINEERS
NABL Accredited as per ISO/IEC: 17025-2005 Laboratory
An ISO 9001 2008 Certified Company

#133, Bhuvaneshwarinagar, Dodda Basti Main Road, Bangalore-560056
e-mail: civilqualityconsultants@gmail.com Ph: 8553518550/9886998316

"TheRoadtoSuccessisalwaysunderConstruction"

NO: CQCE/3rd Party/RRN Division/59/ 2018-19 Date: 15.03.2019

To,
Executive Engineer,
Elctrical – Yelahanka Zone Division
BBMP, Bangalore.

Sir

Sub:- Submission of 3rd Party Report for the work of Providing Path Way Lighting to Bhuvaneshwarinagar Park in Ward No.06, BBMP, Bangalore. - reg.

Ref:- :- (i) Work order No. EE(Elec)/YZ/WO/000015/2018-19 Dated: 21.07.2018
(ii)**Job code No.** 006-18-000065

Adverting to the above, we would like to submit the 3rd Party Inspection Report for the above said work in Electrical – Yelahanka Zone Division along with Mr. Rajendra Nayak(Assistant Executive Engineer, Electrical Yelahanka Zone), and Mr. Kumar (Electrtical Engineer, 3rd Party Consultants), Bangalore on : 14.03.2019

The following works inspected the details of works inspected is as follows,

Sl no	Name of the work	Amount of estimate Rs in Lakhs.	Remarks
1	Providing Path Way Lighting to Bhuvaneshwarinagar Park in Ward No.06, BBMP, Bangalore.	Rs. 10.00 Lakhs (1st and Final bill)	Work carried out satisfactorily Details mentioned in 3rd party compliance report

For details of works and measurements checked during the inspection time in the presence if the officials /officers afore said.

This is for favor of kind information and needful in the matter.

CIVIL QUALITY CONSULTANTS & ENGINEERS Bangalore

Enclosures: 3rd part Inspection report
Thanking you

yours faithfully

Authorized signatory

Office & Laboratory : # 133, Bhuvaneshwarinagar, Dodda Basti Main Road, Bangalore - 560 056.
e-mail:civilqualityconsultants@gmail.com Ph: 080-23240644 / Mob: 8553518550

Name of Work :Providing Path Way Lighting to Bhuvaneshwarinagar Park in Ward No.06, BBMP, Bangalore.

Contractor/Agency	:	Executive Engineer-3, KRIDL, Bangalore.
Name of Client	:	Executive Engineer, Electrical-Yelahanka Zone, BBMP, Bangalore.
Total Bill Cost in Lakhs	:	Rs.8.98Lakhs
Date Of Inspection	:	14.03.2019
Status of Bill	:	First & Final Bill
In the Presence of	:	(a) Mr. Rajendra Nayak(Assitant Executive Engineer, Electrical Yelahanka Zone), BBMP, Bangalore.
	:	(b) Mr. kumar, (Electrical Engineer) M/s Civil Quality Consultants & Engineers, Bangalore.

3rd Party Compliance Report

Sl. No	Description of the Item	Unit	Quantity	Comments / observations
1	Fabricating ,supplying and erection of....Mtrs long hot dip Galvanized Conical pole with BSEN 10025 grade S 355 JO	Each	32	Supplied Material Quality found satisfactory
2	LED Post Top Lantern Gaeden.Supply of LED Post Top Lantern with System..wattage,housing&frame	Each	32	Supplied Material Quality found satisfactory
3	Supplying and fixing electro Mechanical Timer (Without Contactor)using necessary bolts,nuts and Washers etc..	Each	1	Supplied Material Quality found satisfactory
4	Supply and fixing of 4 pole power contactor with NO/NC Contacys on existing wood/panel board using	Each	1	Supplied Material Quality found satisfactory

CIVIL QUALITY CONSULTANTS & ENGINEERS Bangalore

5	Supplying and fixing miniature circuit breakers on existing MCB distribution boards using necessary fixing materials.....	Each	4	Supplied Material Quality found satisfactory
6	Wiring for Lighting/power circuit using one of PVC insulated 1100v grade,multis and copper conductor single core cable.....	P/Mtr	10	Supplied Material Quality found satisfactory
7	1.5 Sqmm	P/Mtr	192	Supplied Material Quality found satisfactory
8	Supplying,fixing,wiring,earth electrode for grounding conduits,I.C cutouts and other equipments on the meter board	Each	1	Supplied Material Quality found satisfactory
9	Supplying and fixing of porcelain fuse channel with cut out on existing wooden/panel using necessary nuts bolts	Each	3	Supplied Material Quality found satisfactory
10	Supplying and fixing of class A (Medium duty)GI pipe of Wall thickness not less than 3.25mm on Pole/Wall.....	P/Mtr	6	Supplied Material Quality found satisfactory
11	Fabricating supplying and mounting MS Box made out...SWG Suitable for Floor Wall mounting,fully weather Proff with Provision.....	Sqcm	29650	Supplied Material Quality found satisfactory
12	Supplying and fixing angle iron frame work fabricated out of M.S angle iron....And M.S Flat	P/Mtr	5	Supplied Material Quality found satisfactory
13	Supplying and running of GI/Copper strips for grounding Connections,using Necessary fixing materials as required.....	P/Mtr	5	Supplied Material Quality found satisfactory
14	Supplying of 1.1 KV LT UG cable having aluminium conductor PVC insulated	Each	2	Supplied Material Quality found satisfactory

CIVIL QUALITY CONSULTANTS & ENGINEERS Bangalore

15	Supplying and Fixing L.T Cast iron pot heads suitable for 1.1 KV Class UG Cable filled with	P/Mtr	556	Supplied Material Quality found satisfactory
16	3.5 Core 25 Sqmm	P/Mtr	50	Supplied Material Quality found satisfactory
17	Labour charges for laying of 1.1 KV class UG cable in existing trench GI pipe/stoneware pipe / on Wall on poles as required.....	P/Mtr	556	Supplied Material Quality found satisfactory
18	3.5 25Sqmm to 75 Sqmm	P/Mtr	50	Supplied Material Quality found satisfactory
19	Digging of trench of 0.6m deep x 0.50 mtr wide refilling thr trench to yhe required ground level.....	P/Mtr	500	Supplied Material Quality found satisfactory
20	Providing RCC Pole pedstal of Size 0.3x0.3x0.8 Mtrs including digging of Pit,tor steel,Anchoring bolts	Each	32	Supplied Material Quality found satisfactory

Verified By

CIVIL QUALITY CONSULTANTS & ENGINEERS Bangalore

Authorised Signatory

For CIVIL QUALITY CONSULTANTS & ENGINEERS

Authorised Signatory

Providing Path Way Lighting to Bhuvaneshwarinagar Park in Ward No.06, BBMP, Bangalore.

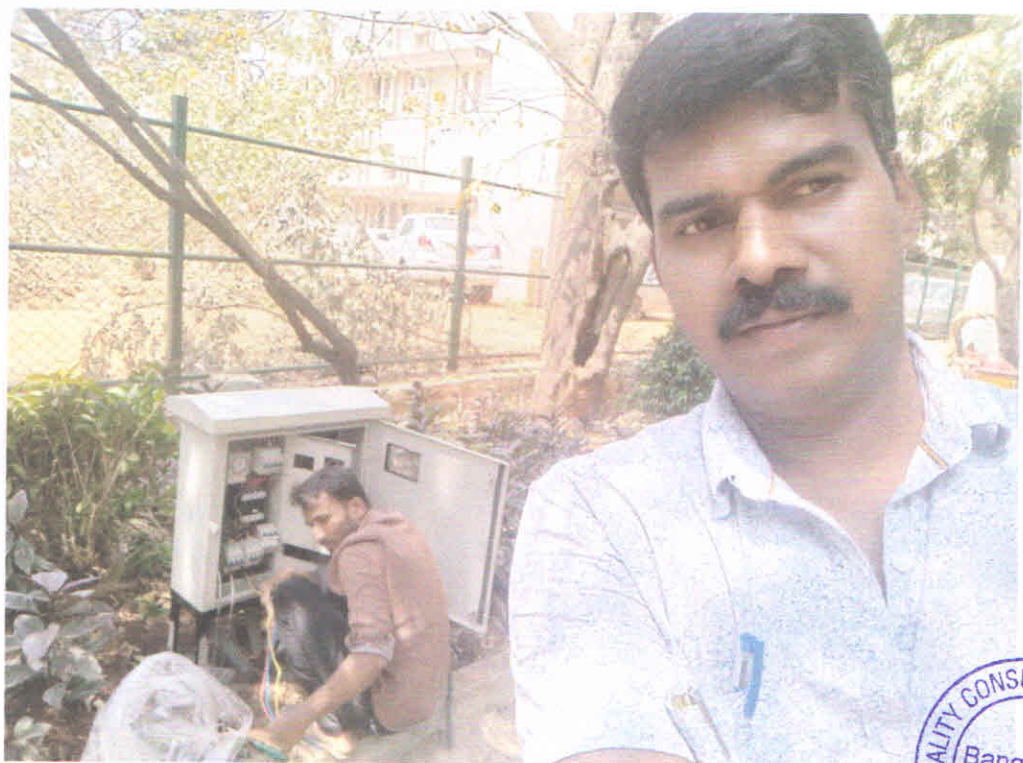

CIVIL QUALITY CONSULTANTS & ENGINEERS
Bangalore

Providing Path Way Lighting to Bhuvaneshwarinagar Park in Ward No.06, BBMP, Bangalore.

CIVIL QUALITY CONSULTANTS & ENGINEERS
Bangalore
